

TECHHUB ELECTRONICS

IMPLEMENTATION PLAN

A controlled 36-month path to connected omnichannel retail

Purpose Translate the approved transformation roadmap and technology assessment into an executable work breakdown, critical path, resource and budget baseline, quality gates, phased go-live controls and sustainable support model.

Prepared by: Shanaka Pradeep Govinna

Prepared for the Executive Steering Committee
Final version | 10 September 2026

Delivery window: January 2027-December 2029 | Budget: AU\$18.6m

EXECUTIVE BRIEF

Contents and executive summary

Section	Page
1. WBS, scope and task detail	3-5
2. Resource allocation	6
3. Timeline and critical path	7
4. Governance and budget	8-9
5. Risk management	10
6. Quality and testing	11
7. Go-live strategy and rollback procedures	12
8. Post-implementation support and benefits	13

Executive decision

Approve a stage-gated implementation beginning in January 2027. Configure and integrate commercial platforms rather than custom-building the core: Dynamics 365 Commerce/Store Commerce; Commerce Distributed Order Management and Inventory Visibility; Dynamics 365 Supply Chain Management WMS; Azure integration, identity and monitoring; and Power BI/Fabric. Defer a full ERP replacement. Treat CRM as a conditional customer-service, consent and loyalty capability released only if the Month 1-3 fit-gap shows current tools cannot meet the approved service journeys.

36 months Jan 2027-Dec 2029	AU\$18.6m approved envelope	65 stores wave rollout	6 gates evidence before scale
--------------------------------	--------------------------------	---------------------------	----------------------------------

1. WORK BREAKDOWN STRUCTURE

1.1 Project Structure

The hierarchy below retains the template structure and expands it to the approved TechHub delivery scope

WBS branch	Child work packages	Purpose / scope control
1.0 Project Initiation	1.1 Project Charter 1.2 Team Formation 1.3 Stakeholder Kickoff 1.4 Discovery and Current-State Analysis 1.5 Requirements Validation 1.6 Technology and Interface Assessment 1.7 Assurance Planning 1.8 Gate 1 Approval	Mobilise governance, people, requirements, process baselines, architecture evidence and approvals before major commitments.
2.0 Technology Implementation	2.1 CRM / Customer-Service Integration (conditional) 2.2 ERP Fit-Gap and Core-System Integration 2.3 E-commerce Enhancement 2.4 POS Modernisation and Store Enablement 2.5 OMS and ATP Implementation 2.6 WMS and Warehouse Enablement 2.7 API, Master Data and Monitoring 2.8 BI, Demand Planning and Personalisation	Deliver the approved connected-retail capabilities. Full ERP replacement is deferred; CRM funding is released only when Gate 1 confirms the need.
3.0 Change Management	3.1 Communication Execution 3.2 Training and Readiness Delivery 3.3 Support Implementation	Prepare affected employees and customers, prove readiness and establish support for every release wave.
4.0 Project Closure	4.1 Go-Live and Hypercare Support 4.2 Knowledge Transfer and BAU Handover 4.3 Project and Benefits Review	Stabilise services, transfer ownership, confirm benefits and formally close the programme.

Approved requirement alignment

Requirement	Primary WBS coverage	Required outcome
R1 Website	2.3, 2.5, 2.7	Accessible search-to-return journey with secure payment and reliable promises
R2 OMS/ATP	2.5, 2.7	Reservations, routing, delivery/collection and common order status
R3 WMS	2.6, 2.7	Scan-directed warehouse execution, serial control and accurate inventory
R4 Store/service	2.1, 2.4, 2.5	Consistent order, stock, collection and return visibility
R5-R7 Enablers	2.7, 2.8, 3.0	Trusted data/APIs, security, reporting, training, support and adoption

Scope clarification The supplied CRM and ERP headings are retained but corrected to match the approved plan: CRM is conditional customer-service/consent/loyalty integration, and ERP work is fit-gap plus integration—not a full ERP replacement.

1. WORK BREAKDOWN STRUCTURE

1.2 Detailed Task List

Initiation and foundation tasks

Task ID	Task Name	Duration	Dependencies	Resource	Start Date	End Date
1.1.1	Develop project charter, governance, controls and integrated plan	1 month	None	Programme Director	01 Jan 2027	31 Jan 2027
1.2.1	Form core team; confirm workstream leads, capacity and backfill	1 month	1.1.1	Programme Director	01 Jan 2027	31 Jan 2027
1.3.1	Conduct stakeholder kickoff and confirm engagement cadence	1 month	1.1.1, 1.2.1	Sponsor / Lead BA	01 Jan 2027	31 Jan 2027
1.4.1	Interviews, store/DC observation, current-state maps and baselines	3 months	1.3.1	Lead BA / Process Owners	01 Jan 2027	31 Mar 2027
1.5.1	Requirements catalogue, NFRs, traceability and signed priorities	3 months	1.4.1	Product Owners	01 Jan 2027	31 Mar 2027
1.6.1	Application, interface, volume, licence and supportability inventory	3 months	1.2.1	Enterprise Architect	01 Jan 2027	31 Mar 2027
1.7.1	Privacy impact, PCI scope, threat model and accessibility plan	3 months	1.5.1	Risk & Security Lead	01 Jan 2027	31 Mar 2027
1.8.1	Vendor fit-gap, CRM/ERP decisions and Gate 1 baseline approval	3 months	1.4.1-1.7.1	Steering Committee	01 Feb 2027	30 Apr 2027
2.2.1	ERP fit-gap, core records, finance postings and interface decisions	4 months	1.6.1, 1.8.1	Enterprise Architect	01 Feb 2027	31 May 2027
2.7.1	Target process, architecture, environments and release design	4 months	1.5.1, 1.6.1	Architecture Board	01 Feb 2027	31 May 2027
2.7.2	Product, price, location, customer, stock and order ownership	4 months	1.4.1	Data Council	01 Feb 2027	31 May 2027
2.7.3	Canonical schemas, API standards, event model and security patterns	5 months	2.7.1, 2.7.2	Integration Lead	01 Feb 2027	30 Jun 2027
2.7.4	Azure API/event platform, CI/CD, test environments and monitoring	7 months	2.7.3	Platform Lead	01 Mar 2027	30 Sep 2027
2.7.5	Data profiling, cleansing, matching, migration waves and rehearsal	9 months	2.7.2	Data Lead	01 Mar 2027	30 Nov 2027
3.3.1	Service model, release calendar, test strategy and support design	4 months	1.8.1	Programme Director	01 Mar 2027	30 Jun 2027

Definition of done for foundation

Gate 2 at Month 9 requires approved designs, environments, service monitoring, reconciled migration rehearsal, contract deliverables, budget forecast, trained delivery teams and no unresolved critical privacy/security architecture finding. Microsoft platform prerequisites and service boundaries are verified in the tenant before configuration (Microsoft, 2026a, 2026b).

1. WORK BREAKDOWN STRUCTURE

1.2 Detailed Task List — continued

Technology delivery, change and closure tasks

Task ID	Task Name	Duration	Dependencies	Resource	Start Date	End Date
2.3.1	Commerce UX, content/search prototype and accessibility validation	4 months	1.5.1	Digital Product Owner	01 Jan 2027	30 Apr 2027
2.3.2	Commerce build: checkout, payment, accounts, tracking and returns	7 months	2.7.1, 2.7.4	Commerce Lead	01 Apr 2027	31 Oct 2027
2.5.1	OMS status, ATP, reservations, routing, notifications and returns	11 months	2.7.1, 2.7.4	Order Product Owner	01 Mar 2027	31 Jan 2028
2.3.3	Commerce/OMS controlled release and optimisation	26 months	2.3.2, 2.5.1	Digital Product Owner	01 Nov 2027	31 Dec 2029
2.6.1	Warehouse process redesign; Wi-Fi, devices and labels	8 months	1.4.1	DC Operations Lead	01 Jan 2027	31 Aug 2027
2.6.2	Item, location and serial master cleanse; cutover preparation	8 months	2.7.2, 2.6.1	Data + DC Leads	01 Apr 2027	30 Nov 2027
2.6.3	Configure/integrate WMS inbound, stock, outbound and returns	8 months	2.7.3-2.7.5	WMS Lead	01 Apr 2027	30 Nov 2027
2.6.4	Distribution-centre pilot, stabilisation and rollout	14 months	2.6.1-2.6.3	DC Operations Lead	01 Nov 2027	31 Dec 2028
2.4.1	POS/service fit-gap; order, stock, return view and receipts	8 months	1.8.1, 2.7.4	Store Product Owner	01 Jun 2027	31 Jan 2028
2.4.2	Store task queues, scanning, staging and collection proof	8 months	2.5.1, 2.4.1	Store Operations Lead	01 Aug 2027	31 Mar 2028
2.4.3	Representative-store pilot and rollout across 65 stores	16 months	2.6.4, 2.4.2	Retail Director	01 Feb 2028	31 May 2029
2.1.1	Conditional CRM, service, consent and loyalty integration	24 months	1.8.1, 2.7.2	Service Product Owner	01 Jun 2027	31 May 2029
2.8.1	Dashboard model, baselines and data-quality reporting	12 months	2.7.2-2.7.5	BI Product Owner	01 Jan 2027	31 Dec 2027
2.8.2	Order, stock, service and benefits dashboards	15 months	2.5.1, 2.6.3, 2.8.1	BI Lead	01 Oct 2027	31 Dec 2028
2.8.3	Demand-planning pilot, back-test and planner approval	13 months	2.8.2	Planning Director	01 Dec 2028	31 Dec 2029
3.1.1	Execute communication for stakeholders and rollout waves	36 months	1.3.1	Change Manager	01 Jan 2027	31 Dec 2029
3.2.1	End-to-end tests, role training, readiness and rehearsals	22 months	All releases	Test + Change Leads	01 Aug 2027	31 May 2029
3.3.2	Implement support, monitoring, runbooks and escalation	29 months	2.7.4, 3.2.1	Service Owner	01 Aug 2027	31 Dec 2029
4.1.1	Provide go-live and wave hypercare support	26 months	Each go-live	Release Manager	01 Nov 2027	31 Dec 2029
4.2.1	Complete knowledge transfer and BAU service handover	19 months	4.1.1	Service Owner	01 Jun 2028	31 Dec 2029
4.3.1	Review benefits, optimisation backlog and programme closure	7 months	4.2.1	Executive Sponsor	01 Jun 2029	31 Dec 2029

Integrated increment A wave is valuable only when product/price, ATP, payment, OMS routing, WMS/store execution, notification, service and return evidence reconcile end to end. Channel-only launches are prohibited.

2. RESOURCE ALLOCATION

2.1 Team Structure

Role	Name/TBD	Responsibility	Allocation %	Skills Required
Project Manager	TBD	Own charter, schedule, budget, risks, vendors, gates and Steering reporting	100%	Programme delivery; retail transformation; budget and vendor management
Business Analyst	TBD	Elicit and analyse requirements; map AS-IS/TO-BE; maintain traceability; support UAT	100%	Workshops; BPMN; requirements engineering; process and data analysis
Technical Lead	TBD	Own architecture, integration, environments, technical quality and deployment design	100%	D365/Azure; APIs/events; security; cloud integration and DevOps
Change Manager	TBD	Assess impacts; execute communications, training, readiness and adoption measurement	80%	Retail change; communications; learning design; readiness and adoption
Test Manager	TBD	Plan and govern system, integration, migration, performance, security and UAT evidence	80%	Test governance; automation; defect control; release assurance
Data & Integration Lead	TBD	Deliver data ownership, cleanse/migration, canonical interfaces, monitoring and reconciliation	100%	Data migration; API integration; master data; SQL; observability
Business Product Owners	TBD by workstream	Prioritise backlog, approve processes and accept business outcomes	50-100%	Commerce, order, warehouse, store, service and BI domain knowledge

2.2 Resource Calendar

Resource	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Project Manager	100	100	100	100	100	100	100	100	100	100	100	100
Business Analyst	100	100	100	100	100	100	100	100	100	80	80	80
Technical Lead	80	80	80	100	100	100	100	100	100	100	100	100
Change Manager	40	40	40	60	60	60	80	80	80	100	100	100
Test Manager	20	20	20	40	40	40	80	80	80	100	100	100
Data/Integration	60	60	60	100	100	100	100	100	100	100	100	100
Product Owners	50	50	50	75	75	75	100	100	100	100	100	100

Calendar values are planned percentage allocations for Year 1 (2027). The Programme Manager maintains rolling 12-month calendars for Years 2-3 using the phase-level demand profile; site champions, warehouse super users and vendor delivery teams are added for their assigned pilot and rollout waves.

3. SCHEDULE

3.1 Master timeline and critical path

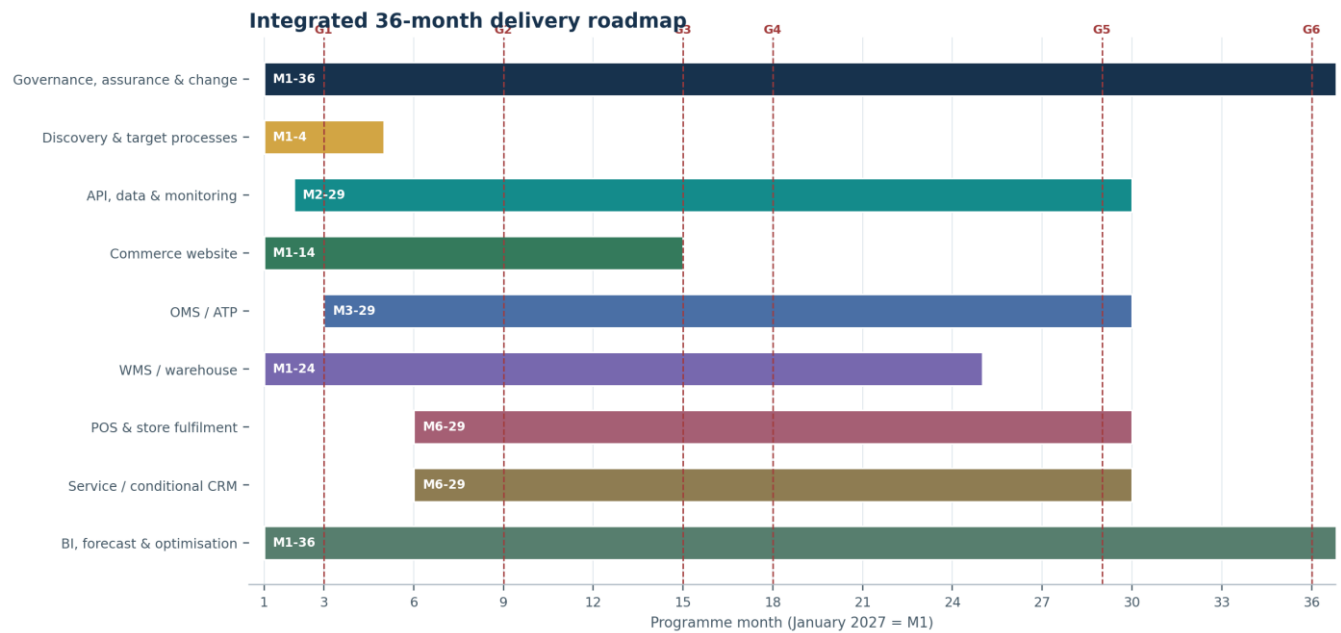


Figure 1. Baseline integrated roadmap. Gate markers: G1 scope/architecture (M3), G2 foundation (M9), G3 first integrated pilot (M15), G4 pilot outcome (M18), G5 scale complete (M29), G6 benefits and handover (M36).

Critical path logic

Critical sequence	Finish	Zero-float condition / recovery lever
CP1 Requirements + process + architecture baseline	M3	Late scope decisions delay contracts and designs; escalate unresolved Must requirements to Gate 1.
CP2 Data ownership + integration foundation	M9	Master-data or event controls block integrated test; add profiling capacity and de-scope noncritical feeds.
CP3 Commerce, OMS and WMS core build	M13	Shared SMEs/environments and defects drive contention; protect release trains.
CP4 Integrated DC/store/customer pilot	M18	Pilot must prove promise-to-fulfil; extend pilot rather than waive accuracy, security or readiness.
CP5 Store rollout + operational transition	M29	Wave rate is constrained by store readiness, training, device/site readiness and support capacity.
CP6 Optimisation, support ownership + benefits closure	M36	Exit requires stable SLAs, accepted runbooks, vendor knowledge transfer and signed benefit evidence.

Control method Maintain a logic-linked schedule with named owners, resource calendars and monthly critical-path recalculation. Track resource-critical constraints as well as logical float; a delayed critical activity moves the programme finish unless an approved recovery plan removes the delay (Project Management Institute [PMI], n.d.).

4. GOVERNANCE

4.1 Milestones, decision rights and stakeholder control

Gate / month	Evidence required	Decision
G1 / M3	Signed scope, process baselines, NFRs, technology fit-gap, CRM/ERP decision, PIA plan, benefits baseline	Approve design/procurement; release conditional CRM allocation only if justified
G2 / M9	Architecture and data controls; integration foundation; migration rehearsal; test/readiness plans; forecast within tolerance	Approve integrated test and pilot preparation
G3 / M15	First integrated pilot evidence; accessibility, PCI, security, reconciliation, DR rehearsal; trained users and support	Go / hold / rollback / extend controlled pilot
G4 / M18	Stable pilot KPIs, store/DC labour evidence, customer feedback, defect trend and residual-risk acceptance	Approve scaled waves and wave cadence
G5 / M29	All active locations in ATP; rollout accepted; SLAs and vendor obligations stable; benefit trajectory	Enter optimisation and BAU transition
G6 / M36	Accepted service, closure audit, benefit realisation, optimisation backlog, contract and data-exit records	Close programme; continue product governance

RACI by control domain

Control	A	R	C / I
Scope, benefits and funding	Executive Sponsor	Programme Director	Steering Committee; Finance; Product Owners
Requirements and acceptance	Business Product Owner	Lead BA / BA team	Process owners; customers; users; QA
Architecture and integration	Architecture Board	Enterprise / solution architects	Security; data; vendors; operations
Data quality and migration	Named Data Owner	Data Lead	Business stewards; solution owners; audit
Security, privacy, PCI, accessibility	Risk Executive	Security / privacy / accessibility leads	QSA; legal; product and test leads
Release and operational readiness	Business Service Owner	Release Manager	Test; change; service desk; vendors

4. GOVERNANCE AND BUDGET

4.2 Financial allocation and control

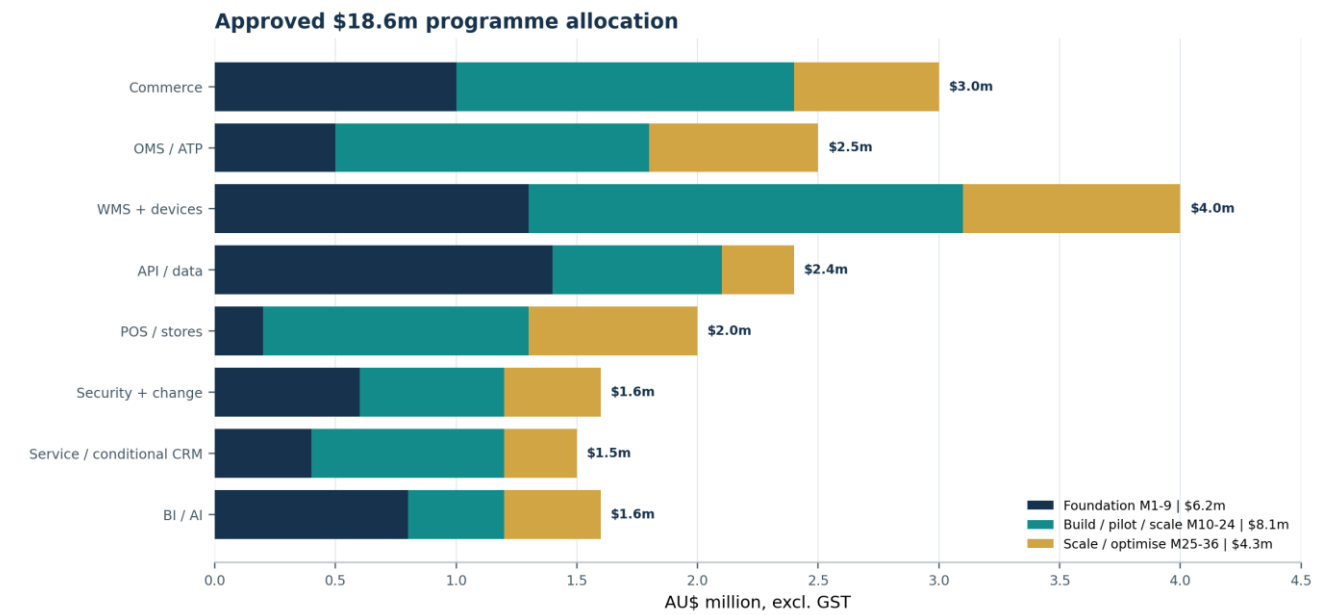


Figure 2. Budget profile by component and phase. Amounts are planning allocations in AU\$ million excluding GST and require RFP validation.

Technology component	M1-9	M10-24	M25-36	Total
Commerce website	1.0	1.4	0.6	3.0
OMS / ATP	0.5	1.3	0.7	2.5
WMS, devices and infrastructure	1.3	1.8	0.9	4.0
API, data, migration and monitoring	1.4	0.7	0.3	2.4
POS and store enablement	0.2	1.1	0.7	2.0
Security, resilience, training and change	0.6	0.6	0.4	1.6
Service, consent and loyalty / conditional CRM	0.4	0.8	0.3	1.5
BI, demand planning and measured personalisation	0.8	0.4	0.4	1.6
TOTAL	6.2	8.1	4.3	18.6

Budget controls

Create cost accounts by WBS and vendor contract. Baseline committed, actual, estimate-to-complete and contingency usage monthly; report variance at completion and benefit impact. A >10% forecast variance at workstream level, any total-envelope breach, or transfer into the conditional CRM line requires Steering approval. Unused CRM funding is not automatically spent: it may be returned or redirected to integration/data or store-service risk only through a documented decision. Procurement uses milestone-based payments, acceptance holdbacks, rate cards, licence-volume protections and data/transition exit obligations.

5. RISK MANAGEMENT

5.1 Risk Register

Risk ID	Risk Description	Probability	Impact	Risk Score	Mitigation Plan	Owner
R001	Poor master or migration data reduces inventory and customer trust	4	5	20	Assign data owners; profile, cleanse, rehearse and reconcile every load; pause affected wave	Data Council
R002	Integration latency or event failure produces stale stock or order status	3	5	15	Contract, load and failure tests; retry queue, safe replay, monitoring and continuity procedure	Platform Lead
R003	ATP oversell or incorrect delivery/collection promise	3	5	15	Safety stock, reservation expiry, capacity rules, limited release and rapid disable option	Order Owner
R004	WMS rollout interrupts warehouse receiving or fulfilment	3	5	15	Layout simulation, Wi-Fi/device trial, volume rehearsal, rollback and floor support	DC Director
R005	Payment, privacy or cybersecurity control failure	3	5	15	Minimise PCI/data scope; least privilege; penetration test and incident rehearsal	Risk Executive
R006	Store workload or low employee adoption reduces service and accuracy	4	4	16	Co-design, backfill, task limits, champions, role practice and readiness-based wave pause	Retail Director
R007	Licence, implementation or exchange-rate cost exceeds budget	3	4	12	Validate RFP pricing, volume bands and FX; milestone payments, monthly EAC and contingency control	Finance Lead
R008	Demand forecast model is not trusted or does not improve decisions	3	3	9	Back-test, explainability, planner approval and limited advisory pilot before scaling	Planning Director

6. QUALITY ASSURANCE

6.1 Test strategy, controls and acceptance

Quality layer	Minimum evidence	Exit criterion / owner
Requirements + design	Peer reviews; traceability; prototypes; process simulation; architecture/data/security decisions	100% Must requirements owned and testable / Lead BA
Unit + configuration	Automated unit/config tests, code review, static analysis and deployment evidence	Agreed coverage; no open critical build failure / Solution Leads
API + integration	Contract tests, idempotency, order/status sequencing, retry/dead-letter/replay, negative and failure injection	Golden orders reconcile end to end / Integration Lead
Migration + data	Profiling, duplicates, counts/totals/hash checks, samples, consent and serial/location reconciliation	Signed control totals and exception disposition / Data Owners
System + end-to-end	Search-to-return scenarios across web/POS/OMS/WMS/service/finance including split, cancel and outage cases	100% critical journeys pass / Test Manager
Performance + resilience	Peak/load/soak, failover, restore, backup, network degradation and monitoring tests	SLOs/RTO/RPO demonstrated / Service Owner
Security, privacy + PCI	Threat model, SAST/DAST, penetration, privilege, logging, PIA actions and PCI validation	No critical/high unaccepted finding / Risk Executive
Accessibility	Automated + manual keyboard/screen reader/mobile tests with users with disabilities	WCAG 2.2 AA conformance evidence / Digital Owner
UAT + operational readiness	Role scenarios, SOPs, training, support simulation, cutover and rollback rehearsal	Business/service owners sign acceptance / Release Manager

7. GO-LIVE STRATEGY AND ROLLBACK PROCEDURES

7.1 Go-Live Strategy

Stage	Entry and activity	Exit / decision
Wave 0: rehearsal	Production-like migration, integrations, batch/event replay, DR, support and rollback rehearsal	Timed runbook passes; control totals and roles accepted
Wave 1: controlled pilot	DC cohort, limited commerce traffic and representative stores selected by volume, format, location and readiness	G3/G4 thresholds stable; customer and staff feedback resolved
Wave 2: measured expansion	Cohorts sized to training, device, site, support and fulfilment capacity; feature flags limit risk	Two stable operating cycles and accepted defect/SLA trend
Wave 3: remaining network	Roll across all 65 stores with blackout periods, daily command and local readiness sign-off	All active locations in ATP; business/service acceptance
Optimise + transition	Tune routing, content, labour, dashboards and forecasts; transfer product/service ownership	G6 benefits, knowledge, contracts, controls and backlog accepted

7.2 CCPOLDAT Cutover Readiness Assessment

CCPOLDAT assesses Customer, Channel, Process, Organisation, Location, Data, Application and Technology readiness. Each domain requires accepted evidence before a pilot or rollout wave.

Domain	Required readiness evidence	Accountable owner
Customer	Priority order, collection, delivery, cancellation and return journeys validated; communications and support paths approved	Customer Experience Lead
Channel	Website, POS, store and warehouse touchpoints smoke-tested; feature flags and continuity paths confirmed	Product Owners
Process	End-to-end procedures, cutover runbook, exception handling and manual workarounds rehearsed	Business Process Lead
Organisation	Command roles, decision authority, staffing, training and escalation roster accepted	Programme Manager
Location	DC and wave stores pass device, connectivity, layout, staffing and local-champion checks	Operations Lead
Data	Product, stock, customer, open-order and payment totals reconciled; backup, RPO and migration sign-off complete	Data Lead
Application	Approved versions, configuration, integrations, monitoring, vendor support and restore packages verified	Solution Architect
Technology	Capacity, network, identity, cyber controls, observability and disaster-recovery health checks pass	Technology Lead

Cutover sequence. Freeze unapproved changes at T-14 days; reconcile master data, open orders, stock, backups and the recovery point at T-48 hours; then activate by feature flag after T-0 smoke tests. The Command Lead coordinates 24-hour business, technology, vendor and communication checkpoints.

7.3 Rollback Procedures

Trigger	Immediate containment	Recovery / proof
Duplicate/incorrect payment; material privacy/security event	Stop affected checkout path; preserve evidence; invoke incident plan	Revert payment release/configuration; reconcile every transaction before reopen
Promise/stock error above threshold; event backlog threatens overselling	Disable affected fulfilment option; freeze/release reservations by approved rule	Return to last stable routing/availability version; replay and reconcile events
Order/WMS/POS failure blocks critical trading or fulfilment	Route cohort to legacy/manual continuity path and cap intake	Restore prior application/config version; reconcile orders, stock and financial postings
Store/DC operational or support overload	Pause next wave; reduce feature/store cohort; deploy floor support	Resume only after capacity, training and service metrics recover

Rollback principle Rollback is a business reconciliation, not only a technical restore. Orders, payments, reservations, physical stock, customer communications and finance postings must end in one agreed state with an auditable decision record.

8. SUSTAINMENT

8.1 Hypercare, service transition and benefit realisation

Support tier	Ownership	Planning service target
L1 service desk	Known errors, user help, triage and communication	Sev 1 acknowledge 15 min; Sev 2 30 min; all cases correlated to business journey
L2 product squads	Commerce, OMS, WMS, store/service, data and platform diagnosis	Restore Sev 1 within 4 hours and Sev 2 within 8 hours where continuity path exists
L3 vendors/partners	Product defect, cloud/service escalation and specialist recovery	Contract response/restoration supports TechHub targets; named escalation and RCA
Command / hypercare	First enterprise pilot: six weeks; each later local wave: minimum two weeks	Daily service review until error, volume, SLA, adoption and backlog exit thresholds pass

Operational handover checklist

Accepted service design and CMDB; ownership and on-call roster; dashboards/alerts and business reconciliation; runbooks and known-error records; backups/restore and DR evidence; access recertification; vendor support/exit paths; knowledge sessions and shadowing; licence/capacity forecast; security/privacy/PCI/accessibility evidence; and signed BAU funding. NIST CSF 2.0 Govern, Identify, Protect, Detect, Respond and Recover outcomes frame continuing cyber ownership (National Institute of Standards and Technology [NIST], 2024).

Benefits scorecard

Outcome / Month 36 target	Owner	Frequency and decision use
Digital revenue 20%; website conversion +60%; CSAT +12 points	Digital / CX Directors	Monthly; optimise funnel, content, promise and service
Website >=99.95% availability; key pages meet speed and WCAG 2.2 AA	Digital Service Owner	Real time/monthly; error budget and release gating
All locations in ATP; >=99.5% stock updates; normal updates <=5 min; collection ready >=95%	Order Product Owner	Daily/weekly; routing, safety stock, capacity and exception action
Inventory accuracy >=98.5%; order accuracy >=99.2%; cycle -30%; pick productivity +20%	DC Director	Daily/weekly; process, layout, labour and training action
Store accuracy >=97.5%; employee proficiency/adoption >=90%	Retail + Change Directors	Per wave/monthly; retraining, workload and rollout pace
Inventory turnover +15%; stockouts -40%; forecast pilot beats signed baseline	Planning / Finance	Monthly; human-approved replenishment and benefit validation
