

TECHHUB ELECTRONICS

STAKEHOLDER ANALYSIS & ENGAGEMENT PLAN

People, communication, training and adoption plan for the 36-month transformation

BCS CAPSTONE PROJECT

Prepared by: Shanaka Pradeep Govinna

Final version | 10 September 2026

Contents

Section	Page
Executive summary	2
1. Stakeholder identification	3
2. Impact and readiness assessment	5
3. Communication strategy and timeline	7
4. Change and resistance management	9
5. Training, support and responsibility plan	10

Executive summary

TechHub will modernise its website and connect it with its order, store and warehouse systems. Customers will be able to check stock availability, make secure online card payments, choose delivery or click-and-collect, track orders and complete returns more easily.

The transformation will change the daily tasks, systems and responsibilities of several departments. Warehouse employees, store teams, customer service, digital commerce and IT will experience the greatest change. These groups must be involved early and provided with practical training and ongoing support.

- Manage senior leaders, Finance, IT, digital commerce, warehouse leadership and the programme team closely.
- Keep employees and customers informed in plain language and show how the change affects daily work or service.
- Use ADKAR for overall adoption and SARAH to recognise and respond to employee resistance.
- Measure buy-in through participation, readiness, training completion, correct system use, confidence and unresolved concerns.

1 Stakeholder identification

Stakeholders are grouped by their power to influence the programme and their interest in the outcome. The stakeholder type is an initial assessment and must be checked through interviews during Months 1-3.

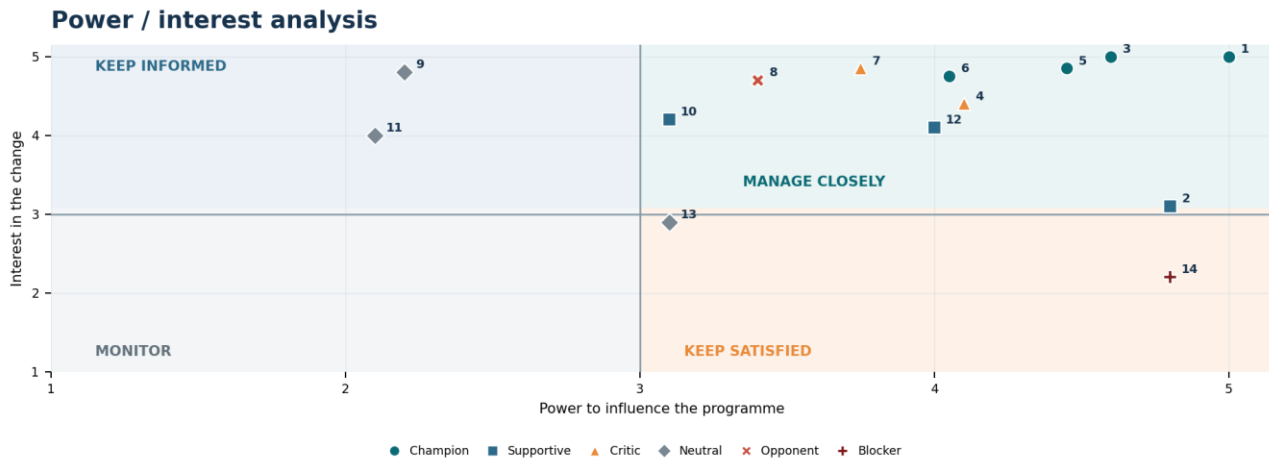


Figure 1. TechHub power and interest analysis. Numbers match the stakeholder register below.

Stakeholder group	Assumed size	Power	Interest	Stakeholder type	Engagement approach	Main concerns
1. Executive steering committee	8 people	High	High	Champion	Manage closely	Cost, benefits, risk and disruption.
2. Board / family owners	5 people	High	Medium	Supportive	Keep satisfied	Return, reputation and long-term value.
3. Programme team	18 people	High	High	Champion	Manage closely	Decisions, resources and dependencies.
4. Finance	22 people	High	High	Critic	Manage closely	Budget, refunds, controls and benefit evidence.
5. IT, data and cybersecurity	35 people	High	High	Champion	Manage closely	Integration, security, recovery and support load.
6. Digital commerce, marketing and customer service	70 people	High	High	Champion	Manage closely	Customer journey, content, conversion and service.
7. Warehouse leaders	12 people	High	High	Critic	Manage closely	WMS design, productivity and go-live continuity.
8. Store managers	65 people	Medium	High	Opponent	Manage closely	Staffing, collection tasks and customer service.
9. Store and warehouse employees	560 people	Low	High	Neutral	Keep informed	Workload, skills, monitoring and job security.
10. Supply chain, procurement and HR	60 people	Medium	High	Supportive	Manage closely	Planning, supplier data, roles and training.
11. Customers	250,000 active	Low	High	Neutral	Keep informed	Privacy, payment security and reliable promises.
12. Technology and payment vendors	8 firms / 25 contacts	High	High	Supportive	Manage closely	Scope, access, delivery and support terms.
13. Suppliers and carriers	160 firms	Medium	Medium	Neutral	Keep satisfied	Data, service standards and connection effort.
14. Regulators and standards bodies	6 bodies	High	Low	Blocker	Keep satisfied	Consumer law, privacy, security and accessibility.

Type meanings: Champion actively leads; Supportive backs the change; Critic challenges constructively; Neutral is not yet committed; Opponent resists; Blocker can stop or delay approval. Types, sizes and power/interest ratings are planning assumptions and must be confirmed in Month 1.

1.2 Detailed stakeholder profiles

Each profile below matches one group in the stakeholder register. Sizes are realistic planning assumptions, not confirmed TechHub figures. The likely attitude is the same as the stakeholder type in Section 1.1 and should be validated during Months 1-3.

Stakeholder group	Assumed size	Current role in organisation	Impact of transformation	Key influencers	Preferred communication methods
1. Executive steering committee	8 people	Provides executive governance, sponsorship and major programme decisions.	Uses new dashboards; approves funding, stage gates, benefits and major exceptions.	CEO, CFO, CIO, COO and programme director.	Monthly decision meetings, dashboards and concise decision papers.
2. Board / family owners	5 people	Approves strategy and major investment; protects long-term business value.	Reviews transformation cost, risk, payback, reputation and strategic outcomes.	CEO, CFO and trusted business advisers.	Quarterly board papers and briefings at funding gates.
3. Programme team	18 people	Coordinates scope, schedule, resources, risks, decisions and workstreams.	Takes responsibility for integrated delivery, change activities and escalation.	Executive sponsor, programme director and workstream leads.	Weekly programme meetings, action logs and daily release contact.
4. Finance	22 people	Controls budgets, payments, refunds, reconciliation, stock value and reporting.	Adopts online-payment controls, connected reconciliation and benefits reporting.	CFO, finance manager, auditors and payment lead.	Monthly finance meetings, control workshops and benefit dashboards.
5. IT, data and cybersecurity	35 people	Maintains applications, infrastructure, data, security and user support.	Designs, integrates, secures and supports the website, OMS, WMS and payment services.	CIO, CISO, solution architect and technology vendors.	Weekly technical workshops, risk reviews and service dashboards.
6. Digital commerce, marketing and customer service	70 people	Manages website content, campaigns, customer enquiries and service messages.	Owns the new online journey, product content, order support and customer communication.	Digital product owner, CX lead and marketing/service managers.	Journey workshops, demonstrations and weekly release briefings.
7. Warehouse leaders	12 people	Controls receiving, storage, picking, dispatch, stock accuracy, staff and safety.	Redesigns warehouse work for WMS and manages pilot continuity and performance.	Operations director, WMS product owner and site champions.	Weekly site workshops, pilot dashboards and readiness reviews.
8. Store managers	65 people	Manages store operations, staffing, customer service and local stock activities.	Adds click-and-collect, returns and order tasks; owns local rollout readiness.	Retail operations lead, regional managers, peers and champions.	Manager calls, demonstrations and weekly rollout briefings.
9. Store and warehouse employees	560 people	Performs POS, replenishment, picking, packing, stock and customer handover tasks.	Uses new scanning, WMS, OMS, collection and returns steps; workload and skills change.	Line managers, super-users, peers and employee representatives.	Shift huddles, hands-on practice, job aids and on-site coaching.
10. Supply chain, procurement and HR	60 people	Plans demand, manages suppliers/contracts, roles, training and employee processes.	Uses connected data, onboards partners and coordinates role and training changes.	Functional directors, change lead, Finance and Operations.	Fortnightly workshops and monthly readiness reports.
11. Customers	250,000 active	Purchases products and uses delivery, collection, support and returns services.	Uses stock availability, secure payment, tracking and simpler returns; privacy matters.	Service experience, store staff, customer reviews and marketing.	Website messages, email, usability research and service updates.
12. Technology and payment vendors	8 firms / 25 contacts	Provides platforms, integration, payment services, implementation and support.	Must meet requirements for security, interfaces, milestones and service levels.	Programme director, procurement lead, integration lead and CISO.	Weekly delivery meetings, formal workshops and service reviews.
13. Suppliers and carriers	160 firms	Supplies products and provides stock, invoice and delivery information.	Provides improved data and delivery updates and meets new connection and service standards.	Procurement lead, logistics lead and contract managers.	Onboarding packs, partner forums and monthly service reviews.
14. Regulators and standards bodies	6 bodies	Oversees consumer, privacy, payment, security and accessibility obligations.	Reviews evidence that legal and standards controls work before launch.	Legislation, industry standards, Legal, privacy lead and CISO.	Formal evidence packs and reviews at design and launch gates.

2 Impact and readiness assessment

2.1 Transformation impact by stakeholder

Impact means the amount of change to work steps, systems, responsibilities and skills. High-impact groups require early involvement, practice and stronger go-live support.

Stakeholder	Process changes	Technology changes	Role / decision changes	Impact and training need
Executive steering committee	Use stage decisions and benefit reviews.	Executive dashboards and decision packs.	Approve scope, funding, gates and major exceptions.	Medium; governance and benefit training.
Board Members	Review investment, return, risk and reputation.	Quarterly board dashboard and papers.	Approve major investment and strategic changes.	Low-medium; concise decision briefings.
Programme team	Coordinate scope, schedule, risks, decisions and change.	Planning, action, risk and reporting tools.	Own integrated delivery and escalation.	High; programme methods and solution overview.
Finance	Reconcile online sales, payments, refunds, stock values and benefits.	Payment, OMS, finance-system and BI data.	Own benefit formulas and financial controls.	High; reconciliation, controls and reporting.
IT / data / cyber	Support connected services, releases, incidents and recovery.	Website, APIs, OMS, WMS, identity, monitoring and security tools.	Take permanent ownership after handover.	Very high; solution, support and security skills.
Digital / marketing / service	Manage the journey, content, campaigns, order support and customer messages.	Commerce, product data, CRM/OMS and analytics.	Own customer outcomes, content quality and service.	High; platform, content, privacy and order lifecycle.
Warehouse leaders	Redesign receiving-to-dispatch and stock-count processes.	WMS dashboards, devices and OMS status.	Own accuracy, productivity, safety and adoption.	Very high; process control and WMS management.
Store managers	Plan collection/returns work and monitor service and stock accuracy.	Connected POS/OMS, task lists and dashboards.	Own local readiness, capacity and exception decisions.	High; workflow, coaching and performance use.
Store and warehouse employees	Use scanning, fulfilment, collection, returns and stock steps.	Handheld WMS and connected POS/OMS screens.	Complete tasks correctly and report exceptions.	Very high; repeated hands-on role training.
Supply chain / procurement / HR	Use demand and stock data, manage partners, roles, training and consultation.	Planning, purchasing, supplier and learning reports.	Own planning controls, people readiness and supplier requirements.	High; data, process, change and facilitation skills.
Customers	Use improved shopping, payment, delivery, collection, tracking and returns.	Website, account, notifications and payment gateway.	Provide research and pilot feedback.	Medium; clear guidance, not formal training.
Technology / payment vendors	Build, connect, test and support the selected services.	Vendor platforms, APIs, payment and monitoring tools.	Meet scope, security, milestones and service levels.	High; TechHub processes, controls and support procedures.
Suppliers and carriers	Provide better product, stock and delivery data.	Partner feeds, portals, APIs and delivery updates.	Meet data and service requirements.	Medium; partner onboarding and exception procedures.
Regulators / standards bodies	Review evidence of legal and standards compliance.	Compliance reports, test results and control evidence.	Remain independent and require corrective action.	Low; formal briefings and evidence packs.

2.2 Change readiness assessment

The readiness score uses a simple 1-5 scale: 1 = not ready, 2 = limited, 3 = partly ready, 4 = ready with minor actions, and 5 = ready. Scores are estimates until the Month 1-3 baseline is completed.

Stakeholder group	Readiness (1-5)	Readiness factors	Resistance / risk factors
Executive steering committee	4.0	Leadership support and available budget.	Concern about disruption and whether benefits will be realised.
Board / family owners	3.5	Long-term interest and authority over major investment.	May reduce support if cost, risk or payback evidence is weak.
Programme team	3.0	Clear roadmap and decision gates.	Named resources and consistent delivery.
Finance	3.0	Strong control and reporting role.	Benefit baselines, payment design and reconciliation need confirmation.
IT, data and cybersecurity	3.0	Technical knowledge and leadership support.	Legacy connections, data quality and support capacity.
Digital commerce / marketing / service	3.5	High interest in website growth and customer improvement.	Content, order-support, consent and analytics ownership need agreement.
Warehouse leaders	3.0	Clear need for visibility and accuracy.	Exact WMS capability, layout, devices and local capacity unknown.
Store managers	2.5	Customer focus and operational leadership.	Concern about added collection/returns work and staffing.
Store and warehouse employees	2.0	Strong practical process and customer knowledge.	New tasks, digital skill differences, workload and fear of monitoring.
Supply chain / procurement / HR	2.5	Strong product, supplier and people knowledge.	Manual work, uncertain data and unproven change capacity.
Customers	3.0	Demand for convenient online shopping and delivery.	Trust will fall quickly if stock or delivery promises are wrong.
Technology and payment vendors	3.0	Commercial interest and relevant platform skills.	Final scope, access, integration and support commitments are unknown.
Suppliers and carriers	2.5	Existing product and delivery relationships.	Data capability, connection effort and service commitments vary.
Regulators and standards bodies	3.0	Clear external rules and established review processes.	Evidence requirements and control gaps need early confirmation.

2.3 Readiness actions before pilot approval

- Confirm named sponsors, process owners, change leads and local representatives for every store and warehouse in the pilot.
- Measure awareness, confidence, digital skills, workload and perceived risks for each high-impact group.
- Approve future processes, role impacts, training time and the support roster before training starts.
- Require critical groups to reach at least 3.5/5 readiness, at least 95% training completion and no unresolved critical concern before go-live.

3 Communication strategy and timeline

3.1 Communication plan matrix

Messages must answer four questions: why the change is needed, what is changing, when it affects the audience, and what support is available. Communication must be two-way, not only announcements.

Stakeholder	Key messages	Method	Frequency	Responsible party
Board / owners	Investment, risk, progress, benefits and decisions.	Board paper and quarterly briefing.	Quarterly / at gates	CEO / CFO
Steering committee	Progress, decisions, risks, readiness and benefits.	Dashboard and decision meeting.	Monthly; fortnightly near launches	Programme director
Programme / workstream leads	Dependencies, issues, changes and upcoming decisions.	Weekly programme meeting and shared action log.	Weekly	Programme director
Finance	Budget, payment/refund controls and benefit evidence.	Finance working group and gate review.	Monthly / at gates	CFO / benefits lead
IT, data and cyber	Design, data, access, security, recovery and support readiness.	Technical working groups and risk reviews.	Weekly	CIO / CISO
Digital / marketing / service	Journey design, content, release scope, customer messages and feedback.	Demos, workshops and release briefings.	Weekly during build	Digital product owner
Warehouse leaders	WMS design, pilot measures, resources, safety and continuity.	Process workshops, site meetings and dashboard.	Weekly during design/pilot	WMS product owner
Store managers	Click-and-collect, returns, staffing, readiness and customer service.	Manager calls, toolkit, demos and regional meetings.	Monthly; weekly during rollout	Retail operations lead
Store and warehouse employees	Why work is changing, new tasks, timing, training and help routes.	Shift briefings, demonstrations, practice, job aids and huddles.	Monthly; weekly before go-live	Site managers / champions
Supply chain / procurement / HR	Data, supplier needs, role impacts, learning and adoption.	Functional workshops and readiness reports.	Fortnightly	Functional directors
Customers	New features, privacy, payment, delivery/collection and support.	Research, website messages, email and service scripts.	At research, pilot and release	Customer experience lead
Technology / payment vendors	Requirements, interfaces, milestones, security, support and issues.	Formal workshops, delivery meetings and service reviews.	Weekly	Commercial / integration leads
Suppliers and carriers	Product/delivery data, connection needs, service standards and issues.	Partner onboarding, forums and service reviews.	Monthly; weekly during onboarding	Procurement / logistics leads
Regulators / standards	Required evidence for consumer, privacy, payment, security and accessibility controls.	Compliance review and evidence pack.	At design and launch gates	Legal / privacy / CISO

All staff communications should identify a sender, date, affected roles, action required, contact point and next update. Urgent operational messages use the incident process, not the normal newsletter.

3.2 Communication timeline

Timing	Communication activity	Target audience	Key message	Success measure
M1	Programme launch and stakeholder confirmation.	All groups	Why change; scope; what is known and unknown.	Owners confirmed; launch attendance; questions logged.
M1-3	Interviews, surveys and current-process walkthroughs.	Employees, customers and leaders	Your experience will shape the design.	Representative participation; baseline response rate >=70%.
M3-6	Co-design and requirements workshops.	High-impact teams and partners	Agree future work, controls and training needs.	Actions closed; process-owner approval.
M6	Solution and funding decision update.	All internal groups	What was selected, why and what happens next.	Awareness >=90%; misinformation corrected.
M7-10	Website/WMS/OMS demonstrations and role-impact briefings.	Stores, warehouse, service, IT, Finance	See the future process and provide feedback.	Feedback reviewed within 10 working days.
M10-12	Pilot readiness and training campaign.	Pilot users and managers	Training, support, measures and go-live conditions.	Training bookings >=98%; readiness >=3.5/5.
M11-18	Website, WMS and OMS pilot communications.	Pilot staff, customers and partners	Release timing, service changes and issue routes.	Pilot feedback >=80%; no unresolved critical issue.
M13-24	Click-and-collect and store rollout updates.	Store network and customers	What changes by location and how to get help.	Each rollout wave meets communication checklist.
M18-29	65-store rollout and adoption reporting.	All stores and leaders	Progress, lessons, correct use and recognised teams.	Active use >=90%; task compliance >=95%.
M25-34	Forecasting and personalisation briefings.	Planning, marketing, customers, privacy	How data is used and where human approval remains.	Privacy approval; user confidence >=4/5.
M29-36	Handover and benefits communication.	Leaders and permanent support teams	Ownership, results, remaining actions and support.	Owners accept handover; benefits approved by Finance.

4 Change and resistance management

4.1 Change Management Strategy

Change model to use: ADKAR. TechHub will use the Prosci ADKAR model because the transformation depends on people changing daily behaviour, not only installing technology. ADKAR stands for Awareness, Desire, Knowledge, Ability and Reinforcement (Prosci, n.d.).

ADKAR stage	Plain meaning	TechHub actions	Timing	Evidence
Awareness	Understand why TechHub must change.	Share customer, stock, warehouse and website problems in plain language.	M1-6	At least 90% can explain the reason for change.
Desire	Choose to support and participate.	Show role benefits; involve staff in design; address workload and job concerns.	M2-12 and each rollout	Readiness score $\geq 3.5/5$; participation $\geq 80\%$.
Knowledge	Know the new process and system steps.	Role-based learning, demonstrations, job aids and manager briefings.	M6-29	Training completion $\geq 95\%$; assessment $\geq 80\%$.
Ability	Perform the new work correctly.	Practice environment, pilot shifts, coaching and on-site support.	M10-30	Correct use $\geq 90\%$; key task compliance $\geq 95\%$.
Reinforcement	Continue the new way of working.	Adoption reports, recognition, refresher learning and removal of old workarounds.	M13-36 and ongoing	Sustained use; declining errors and support demand.

4.2 Resistance management plan

Resistance model to use: SARAH. TechHub will use SARAH to understand the emotional reactions people may experience during change: Shock, Anger, Resistance, Acceptance and Hope. ADKAR remains the overall adoption framework; SARAH guides the response to resistance. People may move through the stages at different speeds or return to an earlier stage, so managers must use feedback and observation rather than assume a fixed sequence.

SARAH stage	Likely TechHub response	Management action	Timing	Evidence of progress
Shock	Surprise, confusion or uncertainty about the website, OMS, WMS and new work steps.	Announce changes early; explain what, why, when and role impact; provide simple FAQs and demonstrations.	M1-6 and before each wave	Awareness $\geq 90\%$; urgent questions acknowledged within one working day.
Anger	Frustration about workload, job security, monitoring or loss of local control.	Hold listening sessions; respond honestly; explain job and data-use safeguards; record and resolve critical concerns.	M2 onward	No unresolved critical employee-relations issue; sentiment improves.
Resistance	Employees may prefer manual workarounds, doubt stock accuracy or avoid the new systems.	Use representatives and champions; co-design and pilot the process; provide practice time, safe stock buffers and controlled exceptions; remove duplicate work.	M3-29	Participation $\geq 80\%$; readiness $\geq 3.5/5$; approved process use $\geq 95\%$.
Acceptance	Employees understand the benefits but may still need practical confidence.	Provide role-based training, job aids, floor support, coaching, extra attempts and clear escalation routes.	M6-30	Training $\geq 95\%$; assessment $\geq 80\%$; confidence $\geq 4/5$.
Hope	Employees see better customer service, stock visibility and warehouse control and support the new way of working.	Publish results; recognise teams; share improvements; refresh training; retire old workarounds and maintain local support.	M13-36 and ongoing	Correct use $\geq 90\%$; key task compliance $\geq 95\%$; support demand falls.

5 Training, support and responsibility plan

5.1 Training needs by role and department

Training will be based on the work each person performs. Completion alone is not enough: users must practise and demonstrate the required task before access or go-live approval.

Role / department	Current skills	Required skills	Main training gap	Training method
Retail / store operations	POS use and customer service.	OMS order search, ATP availability, collection, returns, stock tasks and customer handover.	New cross-channel tasks and exception handling.	Short classroom/demo, practice and job aids.
Warehouse operations	Receiving, picking, packing and stock knowledge; digital skills vary.	WMS scanning, bin moves, replenishment, dispatch, counts, holds, serial numbers and returns.	System-directed work and accurate scan discipline.	Role-based hands-on training on the warehouse floor.
Supply chain / procurement	Manual forecasting and supplier management.	Demand reports, replenishment suggestions, supplier data and purchasing controls.	Data quality, forecast interpretation and new approvals.	Scenario workshops and guided system practice.
Customer service	Customer enquiries and service policy.	CRM/OMS order view, notifications, returns, refunds, privacy and escalation.	One-case ownership across online/store journeys.	Case simulations, scripts and coached practice.
Marketing / e-commerce	Campaigns and basic website content.	Commerce platform, product content, search, promotions, analytics, consent and testing.	Content governance and measured decisions.	Platform labs, content exercises and analytics workshops.
Finance	Financial control and reporting.	Online payment/refund reconciliation, stock value, benefit formulas and dashboards.	Connected transaction data and benefit evidence.	Control walkthroughs, reconciliation practice and reports.
Information technology	Legacy support and general technical skills.	Commerce/OMS/WMS support, APIs, monitoring, identity, cybersecurity, backup and recovery.	Connected-system ownership and new incident procedures.	Vendor-led technical learning, shadowing and simulations.
Human resources / change	Learning and people processes.	Role-impact tracking, ADKAR, SARAH resistance support, facilitation, readiness, adoption reporting and champion support.	Large-scale change coordination.	Facilitator training, toolkits and coaching practice.
Managers / executives	Functional leadership.	Change sponsorship, decisions, dashboards, benefit ownership and coaching conversations.	Lead adoption and act on evidence.	Briefings, decision simulations and dashboard coaching.

5.2 Training controls

- Managers release employees from normal work for training and practice; attendance is not expected outside paid work arrangements.
- Critical roles complete an assessment and practical task. Users who need more help receive coaching and another attempt.
- Training materials use screenshots, short steps and realistic examples. Accessibility and language needs are checked in Month 3.
- Training data records role, site, course, completion, assessment, access approval and refresher date.

5.3 Training schedule

Training programme	Target audience	Duration	Delivery method	Timeline
Change champion and manager foundation	Managers, HR/change and local champions	1 day + monthly coaching	Workshop and toolkit	M6-8; refresh each wave
Website content and commerce	Digital, marketing and product owners	1-2 days	System lab and content exercise	M8-11
Payment, refunds, privacy and fraud	Digital, Finance, service and IT	Half day	Control walkthrough and scenarios	M9-11
WMS manager / super-user	Warehouse leaders and super users	2-3 days	Classroom, sandbox and floor practice	M9-12
WMS role training	Receivers, pickers, packers, inventory and returns staff	1-2 days by role	Hands-on devices and pilot shifts	M10-15; each rollout wave
OMS / ATP and store fulfilment	Store managers, frontline and service teams	1 day + practice	Demo, sandbox and role scenarios	M10-18; each rollout wave
Technical support and recovery	IT, data and cybersecurity teams	3-5 days + shadowing	Vendor training and incident simulation	M6-18
Finance and benefit reporting	Finance and benefit owners	1 day	Reconciliation and dashboard workshop	M9-14
BI, forecasting and personalisation	Planning, marketing, Finance and data teams	1-2 days	Data workshop and controlled scenarios	M24-30
Refresher and new-starter learning	All affected roles	1-3 hours by role	Micro-learning, coach and assessment	M13-36 and ongoing

5.4 Support model

Support stage	Support provided	Owner
Before go-live	Practice demo system, process rehearsals, job aids, manager briefings, support roster and clear escalation routes, user manuals	Training lead + Core team
Go-live period	On-site floor support, extended help-desk hours, daily huddles, rapid issue triage and visible workarounds approved by process owners.	Site manager + IT/support lead
First four weeks	Enhanced support, daily then weekly adoption review, refresher sessions and closure of high-impact issues, hyper care	Product owner + change lead
Ongoing	Normal help desk, knowledge base, new-starter learning, monthly adoption dashboard and quarterly process improvement.	Permanent business and IT owners

5.5 Change and engagement RACI matrix

R = Responsible for doing the work; A = Accountable for the final decision; C = Consulted before action; I = Informed of progress or decisions. Each activity has one accountable owner.

Activity	Steering	Programme	IT	Digital	Operations	Finance	HR / change
Approve business case, funding and stage gates	A	R	C	C	C	R	C
Define website and customer journey	I	A	C	R	C	C	I
Design OMS and WMS business processes	I	A	C	C	R	C	C
Build integrations, data and security controls	I	A	R	C	C	C	I
Prepare communication and readiness activities	C	A	C	C	C	I	R
Deliver training and go-live support	I	A	C	C	R	I	R
Approve pilot and rollout readiness	A	R	C	C	C	C	C
Monitor adoption and resistance	I	A	C	C	R	I	R
Validate benefits and approve handover	A	R	C	C	C	R	I
